


Narayanghat- Butwal Road Project (West Section)
Km 65+000 to Km 113+535

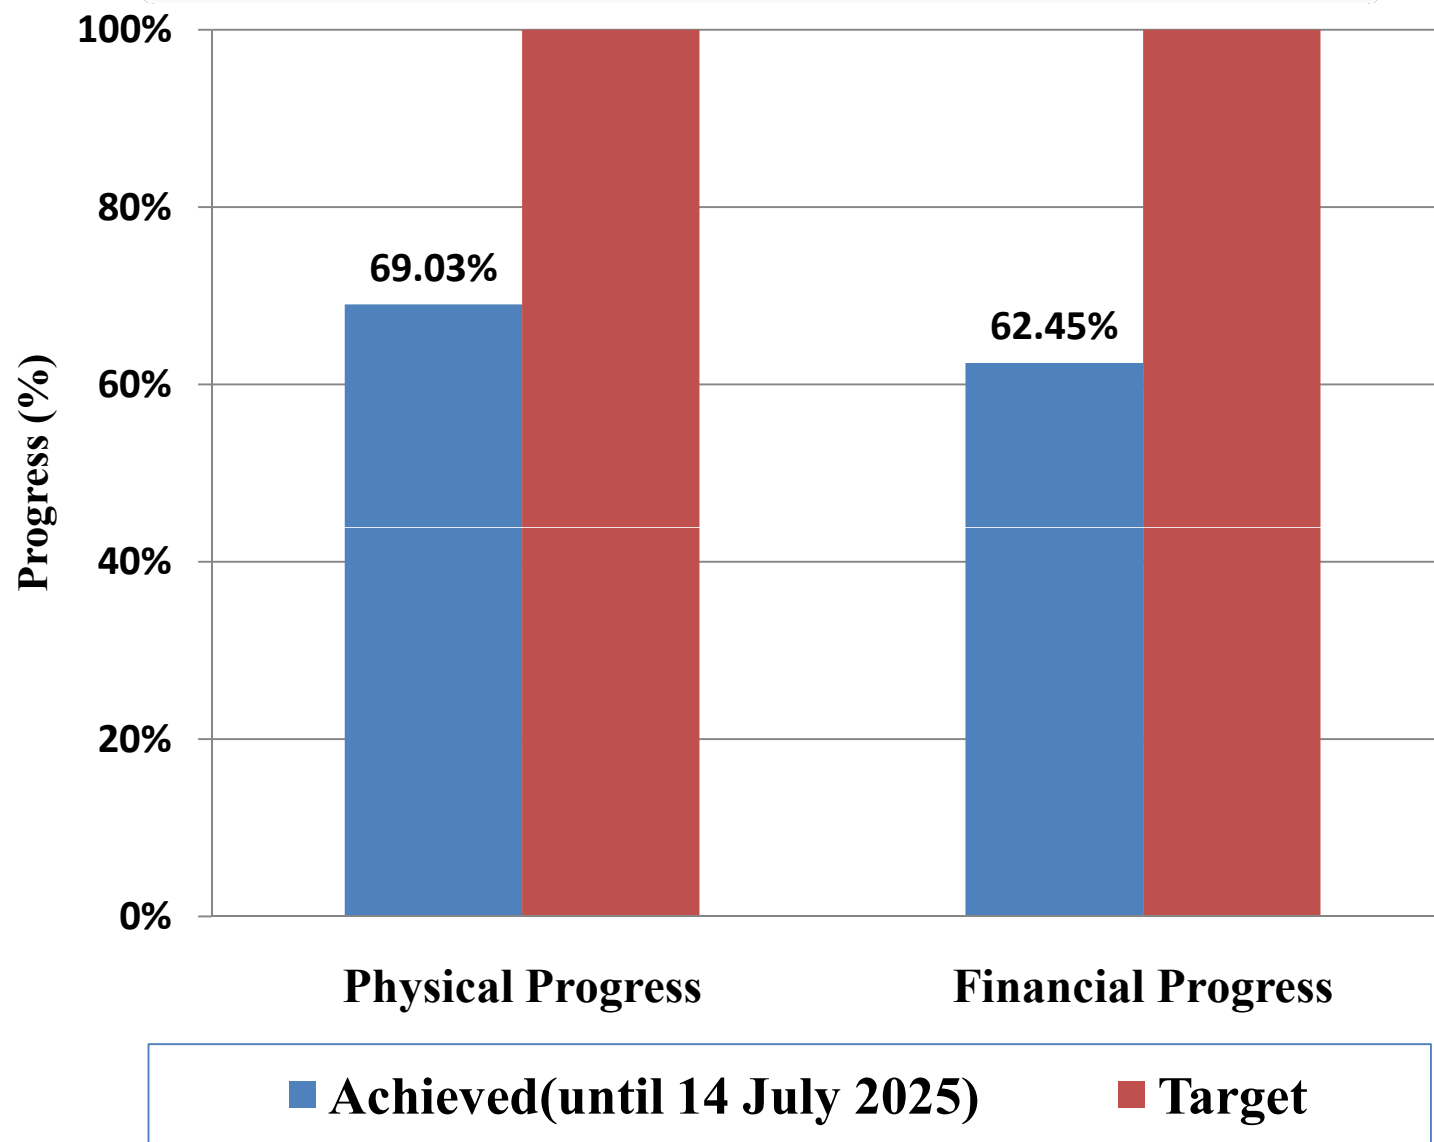

**Work Progress of Major Component on Narayanghat- Butwal Road
Project (West Section) K65+000 to K 113+535 until 14 July 2025**

S.No	Item	Unit	Total Quantity	Work completed	Remark
1	Major Bridges	Nos.	9	8	1 nos ongoing
2	Minor Bridges	Nos.	21	18.5	
3	Box/Slab Culvert	Nos.	258	244	9 nos Ongoing
4	Binder Course	Km	97.07	60.798	One Side of Road Width
5	Wearing Course	Km	97.07	37.625	One Side of Road Width

Major Bridges Work on Narayanghat- Butwal Road Project (West Section) K65+000 to K 113+535 until 14 July 2025

S.No	Major Bridges (Chainage)	Bridge Total length (m)	Remark
1	Bhaluhi Khola Bridge (Chainage - Km 83+345)	66.40	Completed
2	Bhumahi Khola Bridge (Chainage -Km 85+830)	66.40	Completed
3	Somanath khola Bridge (Chainage -Km 90+770)	66.40	Completed
4	Turiya Khola Bridge (Chainage -Km 93+203)	66.40	Completed
5	Kacharar khola Bridge (Chainage -Km 98+260)	51.60	Completed
6	Godhaha Khola Bridge (Chainage -Km 100+948)	66.40	Completed
7	Bhaluhi Khola Bridge (Chainage - Km 104+937)	66.40	Completed
8	Rohini Khola Bridge (Chainage -Km 105+887)	33.20	On Going
9	Sukhaura Khola Bridge (Chainage -Km 110+194)	27.20	Completed
