

नेपाल सरकार

भौतिक पूर्वाधार तथा यातायात मन्त्रालय

सडक विभाग

गुणस्तर अनुसन्धान तथा विकास केन्द्र

सिद्धबाबा सुरुङ्गमार्ग योजना

बुटवल, रुपन्देही - फोन : +९७७-७९-५९९०५३

ईमेल: siddababatunnel79@gmail.com



Government of Nepal
Ministry of Physical Infrastructure and Transport

Department of Roads

Quality Research and Development Centre

Siddhababa Tunnel Project

Butwal, Rupandehi Phone: +97771-591053

email: siddababatunnel79@gmail.com

Date: March 4, 2025 (ने.स.११४५ चित्ला १५ चामुनी ११)

Progress Update of Siddhababa Tunnel Project.

1. Tunnel Excavation Works:

S.N	Tunnel	Total Excavation Length (m)	Update Status		
			From North	From South	Total (m)
1.	Main Tunnel	1089	477.2	610	1089
2.	By Pass 1	151	-	-	151
3.	By Pass 2	161	-	-	161
4.	By Pass 3	130	-	-	130

2. Tunnel Lining Works:



S.N	Tunnel	Total Length (m)	Update Status		
			From North	From South	Total (m)
1.	Main Tunnel Invert	-	250	240	490
1.	Main Tunnel Lining	1126	70	120	190

3. Slope Protection Works:

S.N	Tunnel	Total Area(m ²)	Update Status		
					Total (m ²)

4. Overall Progress:

- Physical: 44.51% (approximately)
- Financial: 43.80 % (Including advanced payment without PS)

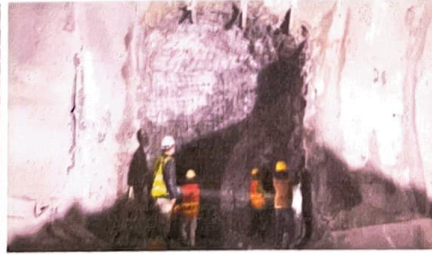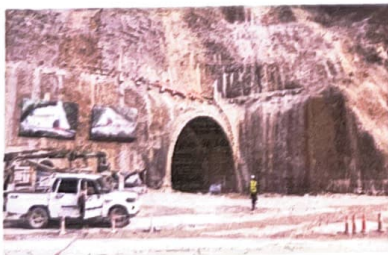

Soumya Anand (Engineer)
Sabita Gyawali (Engineer)
Sushant Upreti (Engineer)
Raj Kumar Pranami (Sub-Engineer)

Krishna Raj Adhikari
2081/11/20

Krishna Raj Adhikari
(Project Manager)

Krishna Raj Adhikari
Project Manager
